


# PROJECT UPDATE

MYCITI PHASE 2A NEWSLETTER

31 MARCH 2026

## The first red bus lanes for Phase 2A

Phase 2A has reached a new milestone with the installation of the first red MyCiTi bus lanes along Govan Mbeki Road, near the Sky Circle project in Lansdowne. Work remains on schedule for completion of the Sky Circle and surrounding roads by December 2026. The distinctive red lanes are dedicated exclusively to MyCiTi buses. With their own lanes and priority at traffic signals, MyCiTi passengers can look forward to faster, more reliable travel compared to using general traffic lanes. The casting of the coloured surface marks a clear sign of progress

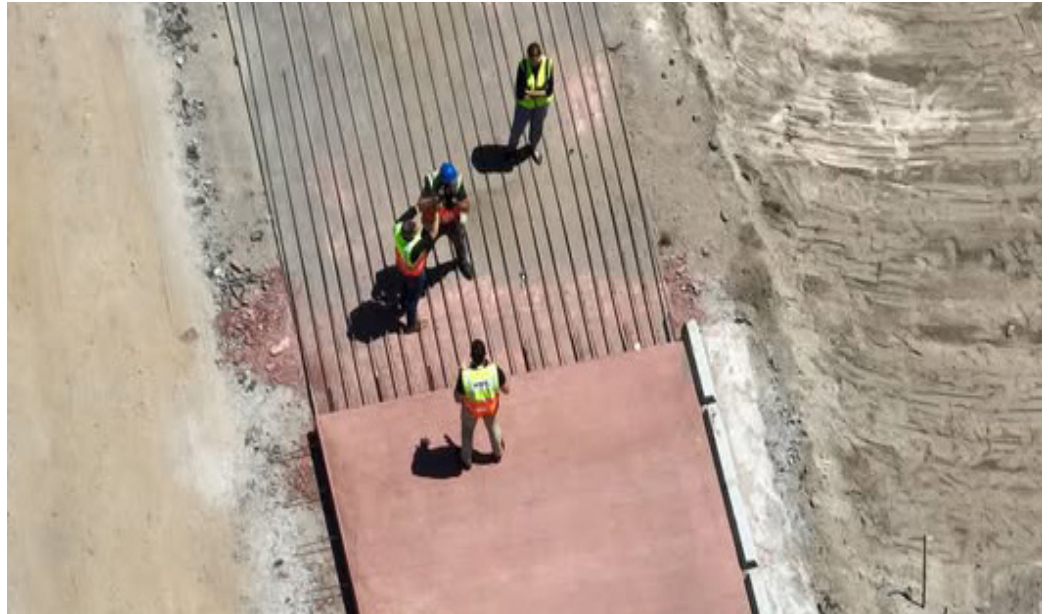

for residents and road users - bringing the improved service one step closer to becoming a reality. Work is now focused on the centre island of the temporary traffic circle

at the intersection of Govan Mbeki Road and Jan Smuts Drive where the concrete is being cast for the overhead structure. Once the circle has been cast and the

concrete has reached its design strength, the temporary traffic circle on ground level will be converted back to a four-way signalised intersection for general traffic.

## Traffic switch underway in Khayelitsha

A traffic switch along Govan Mbeki/ Japhta K. Masemola Roads is underway and will continue for approximately six months to accommodate roadworks between Capital Drive and the Nolungile train station. During this period, the single lane serving traffic towards Khayelitsha will be closed to allow

construction to proceed, while a temporary lane has been established to maintain two-way traffic flow, with one lane open in each direction for both Cape Town-bound and Khayelitsha-bound motorists. Although no full road closures are anticipated, delays should be expected, and motorists are advised to plan ahead and allow extra travel time.



# Construction of Claremont MyCiTi station now underway

Construction has kicked off for the planned MyCiTi station in Claremont, a major destination and key interchange for the planned Phase 2A services. The station will be integrated into the existing public transport interchange (PTI) to create easy connections between different public transport services. A call for public art

proposals was recently undertaken for the station as part of an ongoing commitment to integrating high quality public art into transport infrastructure to uplift the passenger experience while creating an opportunity to celebrate the cultural, historical, and environmental identity of the surrounding communities.



Conceptual illustration showing the entrance design.



## Claremont Boulevard partially closed

Work is progressing along Imam Haron, Chichester and Stanhope Roads. The next phase of roadworks includes the partial closure of Claremont Boulevard until February 2027. The partial closure follows the reopening of the closed lane on the Stanhope Bridge, after the successful remedial works at the retaining wall on the

southeast quadrant. Claremont Boulevard will be affected between Stanhope and Hawthorne Roads:

- The traffic lane from Stanhope Road towards Hawthorne Road will be closed to traffic. A detour will be in place via Station Road and Main Road.
- The traffic lane from Hawthorne Road towards Stanhope Road will remain open.



# Nightworks planned on AZ Berman Drive

Nightworks are planned to take place on AZ Berman Drive in Mitchells Plain, between Nduli Street and Wespoort Drive. Work is planned for approximately eight months from May to December 2026 and is scheduled from Monday to Saturday, between 19:00 and 05:00. Residents can expect some construction related noise during these hours.



## Roadworks in Lansdowne progressing

The extensive construction work along Turfhall Road, between the M5 interchange and the intersection of Castor and Benona Roads is on track for completion in

June 2027. Work is planned to continue between the Castor/Benona Road intersection and the M5 bridge for approximately 10 months.

Noteworthy road closures:

- Crosscut Road will be temporarily closed from April 2026 for approximately 3 months. Prince Arthur Road will temporarily

accommodate traffic in both directions


- The stop-and-go is ongoing on Racecourse Road, between Chukker Road and Stockley Road until the end of June 2026.

## Traffic changes in Gugulethu

There will be an extension of the current temporary traffic layout along Govan Mbeki Road as construction on the transport infrastructure upgrades continues. The existing construction zone between Heinz Road and NY72 Road will shift further along Govan Mbeki Road, with changes

introduced in phases from early March 2026. Lane adjustments at Jakes Gerwel Bridge and near the Vygekraal intersection will remain in place for approximately four months, while the broader temporary layout is expected to stay for eight to twelve months as work progresses. During this period, traffic towards Gugulethu

(eastbound) will be reduced to a single lane from the Jakes Gerwel Bridge. The traffic towards Lansdowne (westbound) will move through a temporary lane shift and reduction from the Vygekraal intersection. Despite these adjustments, two way traffic flow along Govan Mbeki Road will be maintained throughout construction.

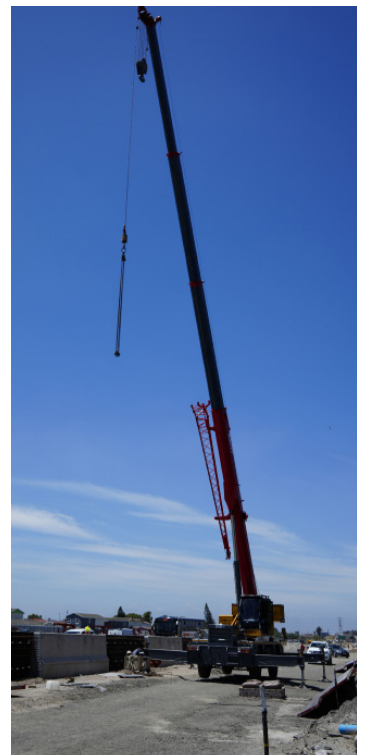

# PARTNERING WITH RESIDENTS

Regular public information sessions are held to keep the public updated on progress and plans, and to provide an opportunity to speak

directly with the project team. The City of Cape Town thanks all residents, businesses and road users for their patience and understanding

during construction as we build and upgrade transport infrastructure to benefit everyone in Cape Town well into the future. Visit our

website and follow us on our dedicated Phase 2 social media channels to stay in touch with the latest news, project updates and public engagements.

## Recent Public Information Sessions

Date	Location	Work Package
10 February 2026	Claremont	W1
26 February 2026	Lansdowne	W2
03 March 2026	Nyanga	E2
04 March 2026	Gugulethu	E2
11 March 2026	Nyanga	E1
12 March 2026	Manenberg	E1
17 March 2026	Claremont (virtual)	W1
24 March 2026	Claremont (virtual)	Bus Facility
25 March 2026	Lansdowne (virtual)	W2
25 March 2026	Mitchells Plain	E6
26 March 2026	Mitchells Plain	E6

## Upcoming Public Information Sessions

Date	Location	Work Package
01 April 2026	Wynberg	Bus Staging Facility
07 April 2026	Khayelitsha	E4
08 April 2026	Khayelitsha	E4
09 April 2026	Khayelitsha	E4
13 April 2026	Mitchells Plain	E6
14 April 2026	Claremont	W1
14 April 2026	Khayelitsha	E4
15 April 2026	Lansdowne	W2

The journey to better public transport

[www.myciti.org.za/Phase2](http://www.myciti.org.za/Phase2)

 MyCiTi Phase 2
  @MyCiTiPhase2
  @MyCiTiPhase2



CITY OF CAPE TOWN'S PUBLIC TRANSPORT SERVICE
